

From:



To:

CC:

Sent:


2/3/2021 3:02:09 PM

Subject:


FW: Draft - SH Project Tracking

Attachments:

Board_System Hardening Project Tracker_Jan 2021.xlsx


I made small changes to the file. So use the one I included here.

On the graph. We need

1. The line that shows where the top 20 % CPZ are, this is because it has to tie back to the definition of the metrics.
 2. Don't need to explain what the blue dots are. Just refer to the line as the risk buydown curve.
 3. The dots to the left of the line are fine
 4. For orange dots to the right of the line – we need to call have a section on the graph explaining why those are there – Fire Rebuild, Cal Trans's Permit, In-Construction.
- 

08W Opportunity Hopper by Phase (Miles)


	Total	Scoping	Estimating	Dependencies	Construc
Total	508.1	433.7	2.9	29.4	42.1

08W Opportunity Hopper (Miles)

	Total	Mitigation Approved	Mitigation Not Approved
Total	508.1	105.3	402.8

08W Opportunity Hopper - Approved Scope by Mitigation Type (Miles)

	Total	Overhead	Underground	Removal	Remote
Total	105.3	79.9	23.0	2.5	0.0

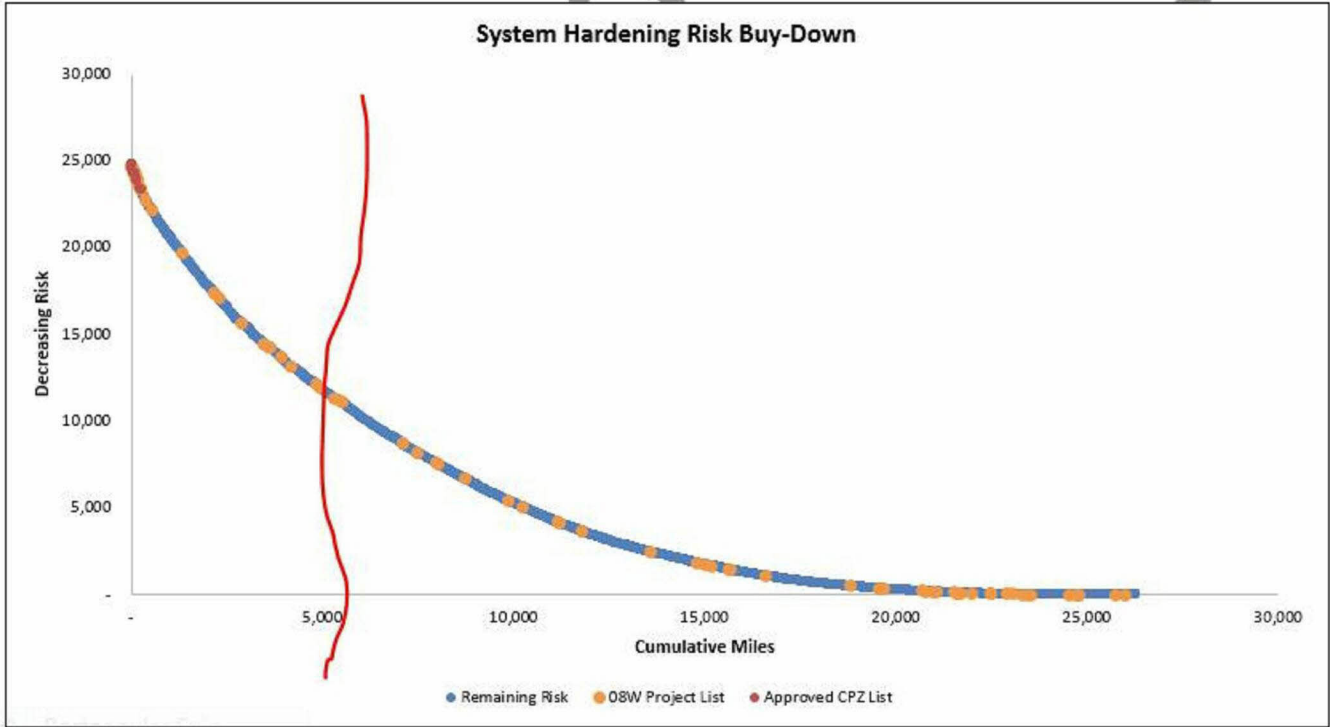

Sup
Ren
buy
Thre

The
repr
goir
proj
for
case

App
whi
scop
whe
hav

[Redacted] | PG&E | Sr. Director, Risk – Special Projects [Redacted]

There is no such thing as a small act of kindness; every act creates a ripple with no logical end.

From [Redacted]
Sent: Wednesday, February 03, 2021 10:12 AM
To: [Redacted]
Subject: RE: Draft - SH Project Tracking

*******CAUTION: This email was sent from an EXTERNAL source. Think before clicking links or opening attachments.*******

[Redacted] – See attached for update System Hardening tracker for the board. We’re working the EVM tracker and will pass that along as soon as we have an updated version.

Thanks,
[Redacted]

kpmg
[Redacted] KPMG LLP
Manager, Strategy
[Redacted]

From: [REDACTED]
Sent: Tuesday, February 2, 2021 10:08 PM
To: [REDACTED]
Subject: [EXTERNAL] FW: Draft - SH Project Tracking
Importance: High

[REDACTED]

This is almost there.

1. Love the summary page
2. Rather than have two tabs, 1 for CPZ and 1 for Projects – Can we merge it. Every Project will have to be associated with a unique CPZ, because we also want to show at the project level. The mitigation chosen – which you have as – OH, UG, RG (Remote Grid / Line Removal)

The # of miles on the CPZ list add up to ~ 1200 miles, should we cull this down to just the 503 miles that will get us the 2021, or is the thought, we are showing ~1200 because the metric is a three year metrics so we want to make sure we have more than ~ 1120 miles teed up for the process.

We can cover this in the morning at 7:30.

Hate to end, but we need something similar for EVM, does not have to have mitigation but something very similar that we can submit to the board.
We then provide monthly updates.

[REDACTED]

[REDACTED] PG&E | Sr. Director, Risk – Special Projects [REDACTED]

There is no such thing as a small act of kindness; every act creates a ripple with no logical end.

From: [REDACTED]
Sent: Tuesday, February 02, 2021 7:30 PM
To: [REDACTED]
Cc: [REDACTED]
Subject: RE: Draft - SH Project Tracking

*******CAUTION: This email was sent from an EXTERNAL source. Think before clicking links or opening attachments.*******

[REDACTED]

See attached for the workbook tracking. We've cleaned it up and will be able to update quickly as the O8W evolves over time.

Three tabs included are:

- **Summary Reporting** – High-level view of the statuses, as of 1/29/2021.
- **Approved CPZs** – Which CPZ's have been approved by the committee for scoping and how many projects / miles are in each (with miles per phase)
- **O8W Project List** – Summarized view of all in the current system hardening pipeline.

Best,

[REDACTED]

kpmg

[REDACTED] KPMG LLP

Manager, Strategy

PGE-DIXIE-NDCAL-000014234

[REDACTED]

From: [REDACTED]
Sent: Tuesday, February 2, 2021 2:42 PM
To: [REDACTED]
Cc: [REDACTED]
Subject: [EXTERNAL] RE: Draft - SH Project Tracking

[REDACTED]

That will work for the meeting. But it will not work for our submission to the board.
For the Board we need to have a more detailed list, an Excel File would be more appropriate.

Anchor on – Circuit Protection Zone and in each CPZ we have a set number of miles.
Within those mile, how many are in each stage – Scoping, Dependency Clearing, ...

- We don't need to call out ECOP, PSPS. As that distinction is irrelevant here.

We have to have it for both SH and EVM as we need to upload it for the Board Materials before Thursday this week.

[REDACTED] | PG&E | Sr. Director, Risk – Special Projects | [REDACTED]

There is no such thing as a small act of kindness; every act creates a ripple with no logical end.

-

From: [REDACTED]
Sent: Tuesday, February 02, 2021 8:54 AM
To: [REDACTED]
Cc: [REDACTED]
Subject: Draft - SH Project Tracking

*******CAUTION: This email was sent from an EXTERNAL source. Think before clicking links or opening attachments.*******

Hey [REDACTED]

Attached are a couple draft slides for the SH meeting today, related to project tracking. These are based on the 08W Status tracking (up-leveled a bit), and there are a few inconsistencies that I'm running down with [REDACTED] and team. Let me know if you have any thoughts and I'll try to work with [REDACTED] to make sure these can get incorporated tonight.

Best,

[REDACTED]

kpmg
[REDACTED] | KPMG LLP
Manager, Strategy
[REDACTED]

The information in this email is confidential and may be legally privileged. It is intended solely for the addressee. Access to this email by anyone else is unauthorized. If you are not the intended recipient, any disclosure, copying, distribution or any action taken or omitted to be taken in reliance on it, is prohibited and may be

PGE-DIXIE-NDCAL-000014235

unlawful. When addressed to our clients any opinions or advice contained in this email are subject to the terms and conditions expressed in the governing KPMG client engagement letter.

CAUTION: This email originated from outside KPMG. Do not click links, open attachments or forward unless you recognize the sender, the sender's email domain and you know the content is safe. Forward suspicious emails as an attachment to US-KPMG SPAM Collection Mailbox [REDACTED]

The information in this email is confidential and may be legally privileged. It is intended solely for the addressee. Access to this email by anyone else is unauthorized. If you are not the intended recipient, any disclosure, copying, distribution or any action taken or omitted to be taken in reliance on it, is prohibited and may be unlawful. When addressed to our clients any opinions or advice contained in this email are subject to the terms and conditions expressed in the governing KPMG client engagement letter.

The information in this email is confidential and may be legally privileged. It is intended solely for the addressee. Access to this email by anyone else is unauthorized. If you are not the intended recipient, any disclosure, copying, distribution or any action taken or omitted to be taken in reliance on it, is prohibited and may be unlawful. When addressed to our clients any opinions or advice contained in this email are subject to the terms and conditions expressed in the governing KPMG client engagement letter.
